

## CHECKLIST 5: Stabilised entranceway

Contractor:	Date:	Consent number:	Site:
	Time:		
Construction checklist		Yes ✓	No ✗ (Add comments to explain)
Check back to 'Stabilised entranceway' section for full information. Also see the Figures over the page.			
Area has been cleared of unsuitable material and smooth graded			
Woven geotextile has been placed over the area, and is properly pinned and overlapped			
At least 10 m of aggregate has been placed (extending from site boundary), 4 m wide and minimum 150mm deep, using 50-150 mm washed aggregate			
Vehicles cannot bypass the entranceway			
Street sweep/suction is done and date recorded			
Inspection and maintenance checks are done, recorded and dated, along with any comments			

Note: this is an on-site, self-check list for contractors to use. Keep your completed checklists to show Compliance Officers your set up, monitoring and maintenance, if requested.


Signature:

# CHECKLIST 5

## FIGURES: Stabilised entranceway



Stabilised entranceway (Source: SouthernSkies)

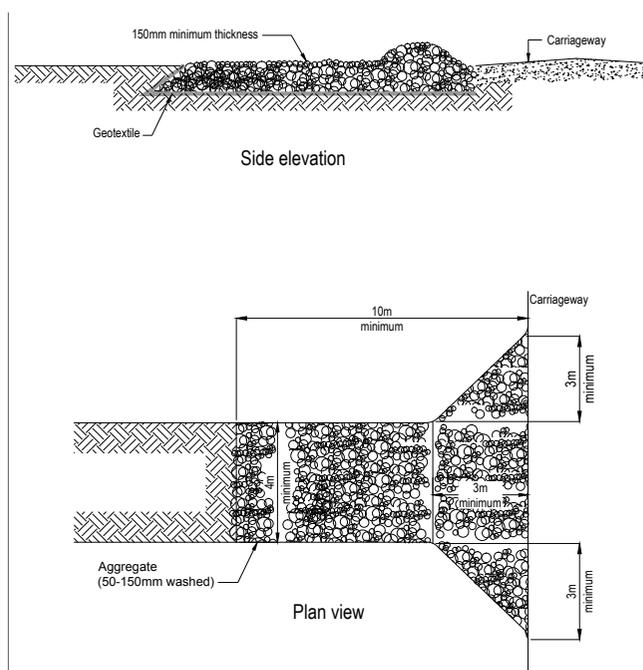

Stabilised entranceway
